



SCARSDALE
PUBLIC SCHOOLS

March 2020 Construction Report



PEC

PARK EAST CONSTRUCTION

Prepared by Francesco V. Borgese



Table of Contents

▶ Section I - Work Progress through the Month of March

Greenacres Elementary School	(Addition and Alterations)
Heathcote Elementary School	(Capital Improvements Project)
Quaker Ridge Elementary School	(Capital Improvements Project)
Scarsdale Middle School	(Capital Improvements Project)

▶ Section II - Planned work for the month of April

▶ Section III - Progress Photos

▶ Section IV - Summary of Daily Reports



Scarsdale Union Free School District Progress Report - Section I Greenacres Elementary School

Work Progress - Greenacres Elementary School Addition (Phase - 1)

- ▶ New addition foundation / footing - Complete
- ▶ New addition CMU partitions - 95% Complete
- ▶ New Addition face brick masonry / Stone Panels - 75% Complete
- ▶ Structural steel erection - 99% Complete
- ▶ 1st floor concrete slab on grade - 99% Complete
- ▶ Installation of 1st and 2nd floor plumbing roughing - 65% Complete
- ▶ Construction of metal frame mansard roof - 60% Complete
- ▶ Installation of concrete plank roofing substrate - 30% Complete
- ▶ Installation of EPDM roofing system - 25% Complete
- ▶ Interior light gauge metal framing 1st and 2nd floor - 70% Complete
- ▶ Installation of 1st floor HVAC duct work - 80% Complete
- ▶ Installation of 2nd floor HVAC duct work - 70% Complete
- ▶ 1st Floor electrical roughing - 80% Complete
- ▶ 2nd Floor electrical roughing - 60% Complete



Scarsdale Union Free School District Progress Report - Section I Greenacres Elementary School

Work Progress - Greenacres Elementary School Addition (Phase - 1)

- ▶ Construction of steel staircase 163 - Complete
- ▶ Roof replacement at existing building - 15% Complete

Work Progress - Greenacres Elementary School Addition (Phase - 2)

- ▶ Installation of new fire alarm system - 50% Complete



**Scarsdale Union Free School District
Progress Report - Section I
HC, QR, MS - Capitol Improvements Project**

Work Progress - Heathcote Elementary School

- ▶ Uploading submittals / shop drawings - 80% Complete

Work Progress - Quaker Ridge Elementary School

- ▶ Uploading submittals / shop drawings - 80% Complete

Work Progress - Scarsdale Middle School

- ▶ Uploading submittals / shop drawings - 80% Complete



**Scarsdale Union Free School District
Progress Report - Section II
Greenacres Elementary School**

**Planned Work for April
Greenacres Elementary School Addition (Phase - I)**

- ▶ Continue plumbing roughing at 1st and 2nd floor.
- ▶ Continue construction of CMU partitions.
- ▶ Continue construction of face brick masonry.
- ▶ Continue construction of light gauge metal frame mansard roofing.
- ▶ Continue installation of concrete roof planking.
- ▶ Continue installation of HVAC ductwork at 1st and 2nd floor.
- ▶ Continue framing interior partitions at 1st and 2nd floor.
- ▶ Continue electrical conduit, boxes, and wire roughing at 1st and 2nd floor.
- ▶ Continue installation of windows.



**Scarsdale Union Free School District
Progress Report - Section I
HC, QR, MS - Capitol Improvements Project**

**Planned Work for April
Heathcote Elementary**

- ▶ Continue to upload submittals / shop drawings.

Quaker Ridge Elementary School

- ▶ Continue to upload submittals / shop drawings.

Scarsdale Middle School

- ▶ Continue to upload submittals / shop drawings.
- ▶ Begin demolition of gymnasium folding partition.
- ▶ Begin exterior masonry repairs.



Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I



Installation of windows at Learning
Commons 146



Installation of windows at
classroom 161



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**




Proposed bathroom plumbing roughing

March 2020




Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I

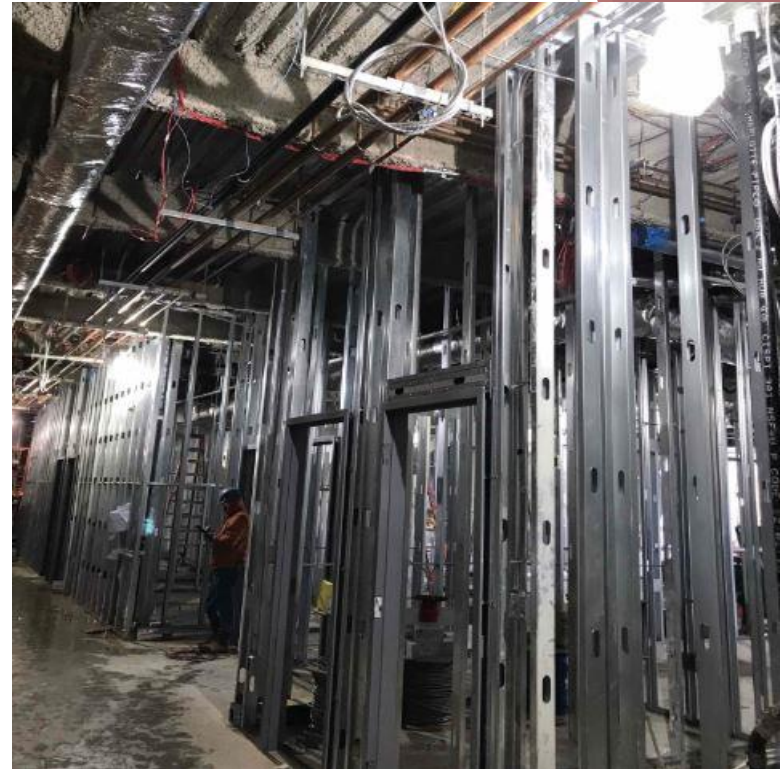

Proposed interior light gauge metal partition framing



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**

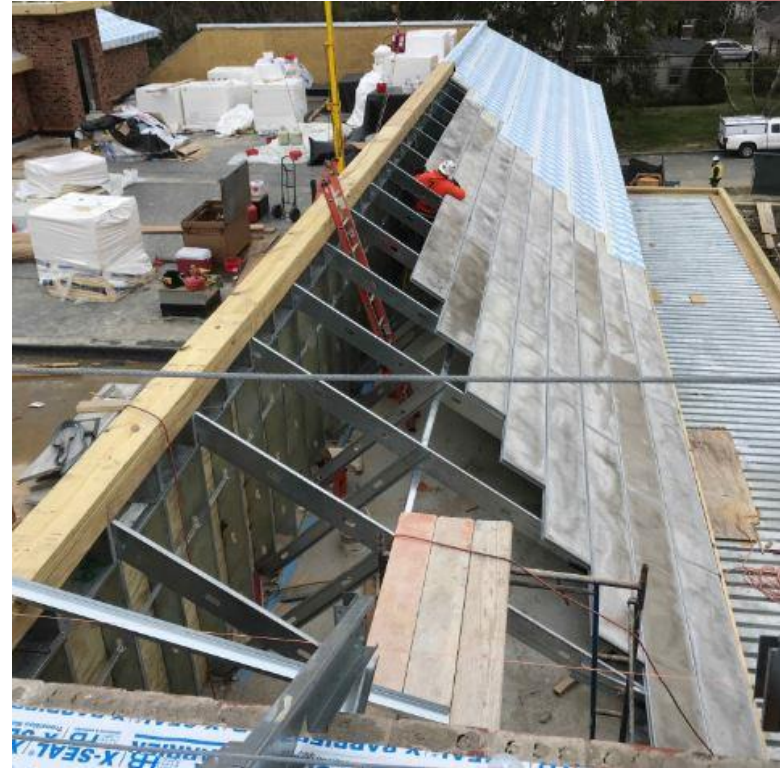

Installation of concrete roof planking

March 2020



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**




Construction light gauge metal mansard roof framing

March 2020



Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I

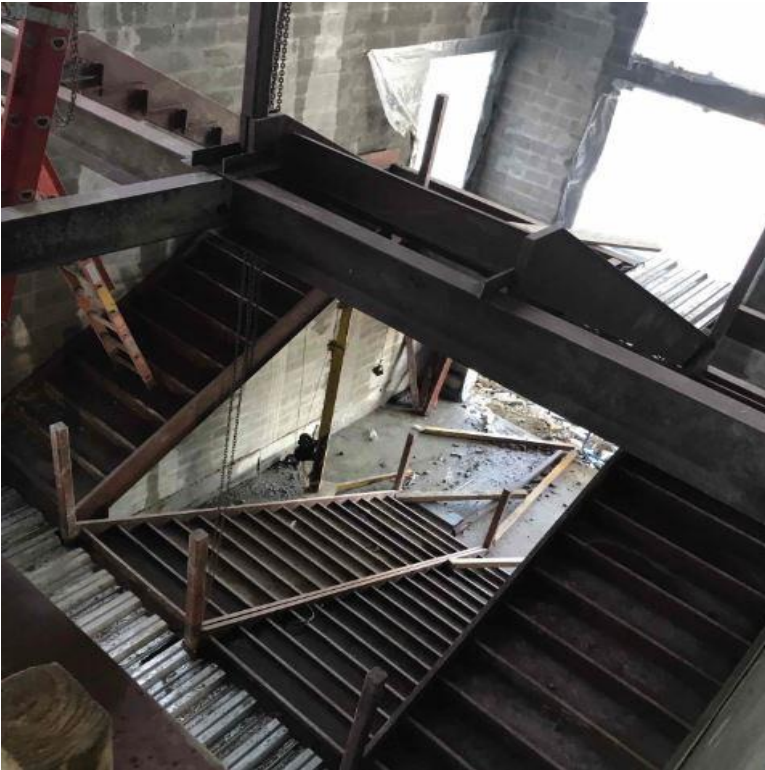

Installation of staircase 163



Installation of staircase 163



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



Replacement of existing roofing
system adjacent to Sage Terrace



Replacement of existing roofing
system adjacent to Sage Terrace

March 2020



Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Phase II



Construction of foundation
formwork and rebar at proposed
stair well 153



Construction of foundation
formwork and rebar at proposed
stair well 153



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Phase II**



Putnam Road exterior elevation




Huntington Avenue exterior elevation



Scarsdale Union Free School District Summary of Daily Reports - Section IV Greenacres Elementary School - Additions & Alterations

Daily Log Manpower Report

▼ MANPOWER GRAPH

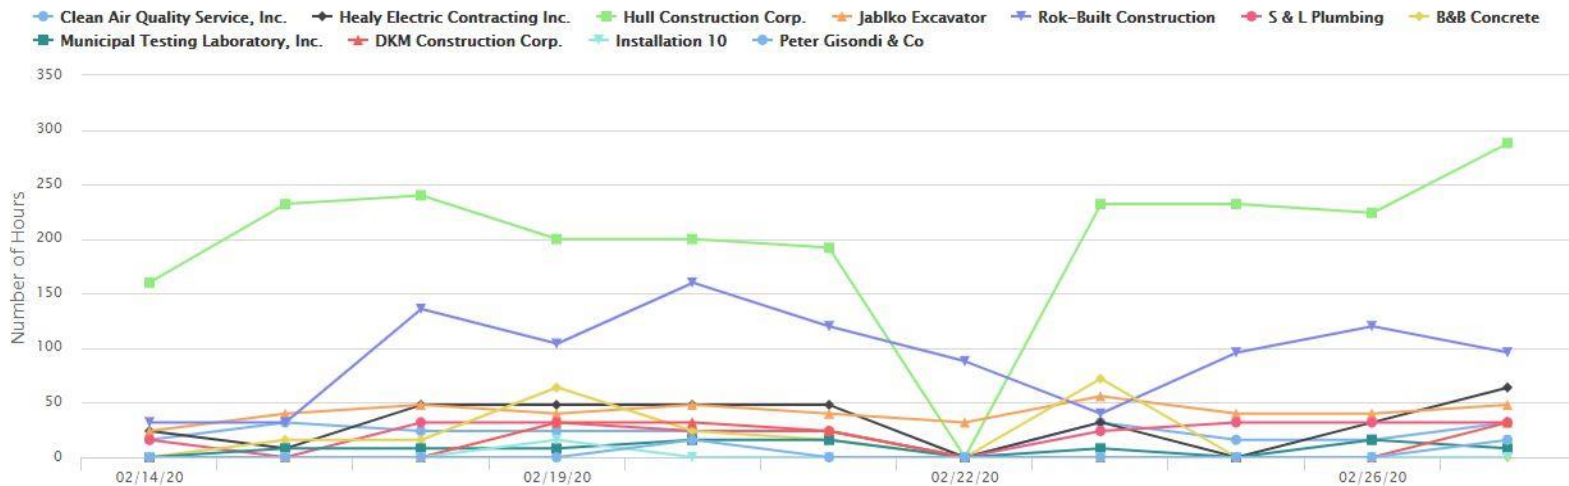

March 2020
