



SCARSDALE
PUBLIC SCHOOLS

May 2020 Construction Report



PEC

PARK EAST CONSTRUCTION

Prepared by Francesco V. Borgese



Table of Contents

▶ Section I - Work Progress through the Month of May

Greenacres Elementary School	(Addition and Alterations)
Heathcote Elementary School	(Capital Improvements Project)
Quaker Ridge Elementary School	(Capital Improvements Project)
Scarsdale Middle School	(Capital Improvements Project)
Edgewood	(HVAC and Interior Alterations)
Fox Meadow	(HVAC and Interior Alterations)

▶ Section II - Planned work for the month of June

▶ Section III - Progress Photos

▶ Section IV - Summary of Daily Reports



Scarsdale Union Free School District Progress Report - Section I Greenacres Elementary School

Work Progress - Greenacres Elementary School Addition (Phase - 1)

- ▶ New Addition face brick masonry / Stone Panels - 95% Complete
- ▶ Installation of 1st and 2nd floor plumbing roughing - Complete
- ▶ Installation of concrete plank roofing substrate - Complete
- ▶ Installation of EPDM roofing system - Complete
- ▶ Interior light gauge metal framing 1st and 2nd floor - Complete
- ▶ Installation of 1st floor HVAC duct work - 95% Complete
- ▶ Installation of 2nd floor HVAC duct work - 90% Complete
- ▶ 1st Floor electrical roughing - 95% Complete
- ▶ 2nd Floor electrical roughing - 95% Complete
- ▶ Roof replacement at existing building - 50% Complete
- ▶ Rigging of HVAC roof top units - Complete
- ▶ Installation of sheetrock wall finish - 50% Complete



Scarsdale Union Free School District Progress Report - Section I Greenacres Elementary School

Work Progress - Greenacres Elementary School Addition (Phase - 2)

- | | |
|---|----------------|
| ▶ Installation of new fire alarm system | - 75% Complete |
| ▶ New gymnasium sky light openings | - 75% Complete |
| ▶ Demolition of existing boilers | - Complete |
| ▶ Demolition of existing classroom finishes | - 25% Complete |
| ▶ Demolition of existing toilet finishes | - 50% Complete |
| ▶ Demolition of existing library finishes | - 20% Complete |
| ▶ Exterior concrete ramp/retaining wall | - 20% Complete |



**Scarsdale Union Free School District
Progress Report - Section I
HC, QR, MS - Capitol Improvements Project**

Work Progress - Scarsdale Middle School

- ▶ Masonry repairs - 30% Complete
- ▶ Demolition of existing gym ceiling - Complete
- ▶ Installation of new gym ceiling 50% Complete



Scarsdale Union Free School District
Progress Report - Section I
Edgewood & Fox Meadow - HVAC & Interior Alterations Project

Work Progress - Edgewood Elementary School

- ▶ Uploading submittals / shop drawings - 80% Complete
- ▶ Construction of attic platforms - 80% Complete
- ▶ Demolition of existing ductwork - 65% Complete
- ▶ Installation of new ductwork within attic - 70%
- ▶ Demolition of existing boilers - Complete

Work Progress - Fox Meadow Elementary School

- ▶ Uploading submittals / shop drawings - 80% Complete
- ▶ Construction of attic platforms - 45% Complete
- ▶ Demolition of existing ductwork - 65% Complete
- ▶ Installation of new ductwork within attic - 30% Complete
- ▶ Demolition of existing boilers - Complete



**Scarsdale Union Free School District
Planned Work - Section II
Greenacres Elementary School**

**Planned Work for May
Greenacres Elementary School Addition (Phase - I)**

- ▶ Continue installation of sheetrock walls.
- ▶ Continue construction of face brick masonry and stone panels.
- ▶ Continue installation of HVAC ductwork at 1st and 2nd floor.
- ▶ Continue electrical conduit, boxes, and wire roughing at 1st and 2nd floor.
- ▶ Continue installation of windows.
- ▶ Continue installation of slate roofing systems.

**Planned Work for May
Greenacres Elementary School Addition (Phase - II)**

- ▶ Receive and begin installation of new boilers.
- ▶ Continue demolition of existing classroom / library finishes.
- ▶ Continue replacement of existing building roofing system.
- ▶ Continue work on existing gymnasium skylight openings.
- ▶ Continue installation of exterior concrete ramp / retaining wall.



**Scarsdale Union Free School District
Planned Work - Section II
HC, QR, MS - Capitol Improvements Project**

**Planned Work for May
Scarsdale Middle School**

- ▶ Continue working on exterior masonry repairs.
- ▶ Continue installation of new gymnasium ceiling.



**Scarsdale Union Free School District
Planned Work - Section II
Edgewood & Fox Meadow - HVAC & Interior Alterations**

**Planned Work for June
Edgewood Elementary School**

- ▶ Continue Uploading submittals / shop drawings
- ▶ Continue construction of attic platforms
- ▶ Continue demolition of existing ductwork
- ▶ Continue installation of new ductwork within attic

Fox Meadow Elementary School

- ▶ Continue uploading submittals / shop drawings
- ▶ Continue construction of attic platforms
- ▶ Continue demolition of existing ductwork
- ▶ Continue installation of new ductwork within attic



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



Photo of Huntington Ave Elevation



May 2020



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



New addition roof.

May 2020



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



Installation of Sheetrock Wall Finishes at 1st Floor of New Addition



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Interior Renovations Phase II**



**Replacement of existing building
roof.**




**Construction of concrete
ramp/retaining wall.**



Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Interior Renovations Phase II



Completion of existing boiler
demolition.

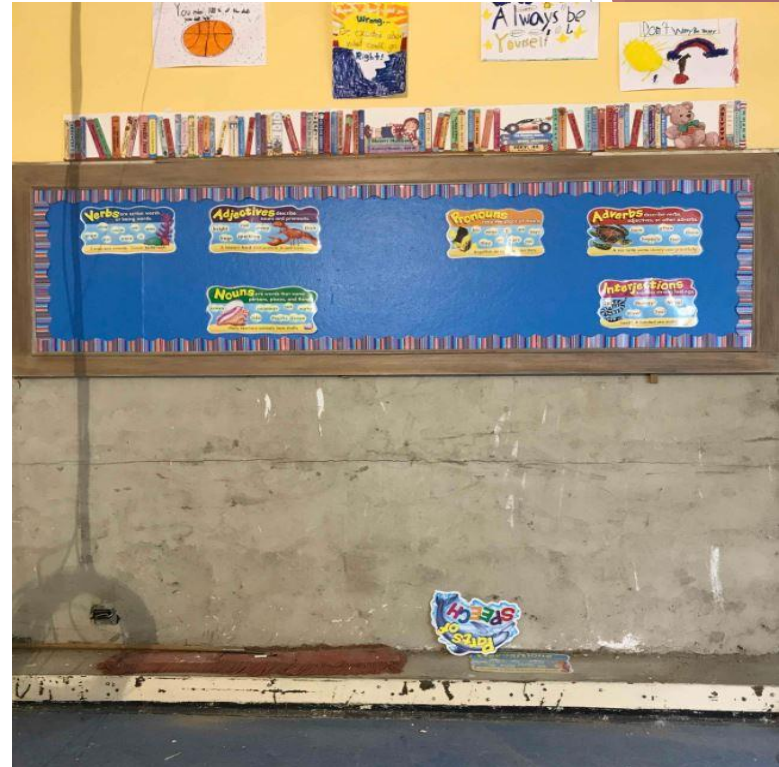

Demolition of existing classroom
finishes.



**Scarsdale Union Free School District
Progress Pictures - Section III
Heathcote, Quaker Ridge, & MS - Capital Improvements**




Installation of new ceiling grid and tiles within Middle School gymnasium.



Scarsdale Union Free School District Summary of Daily Reports - Section IV Greenacres Elementary School - Additions & Alterations

Daily Log Manpower Report

▼ MANPOWER GRAPH

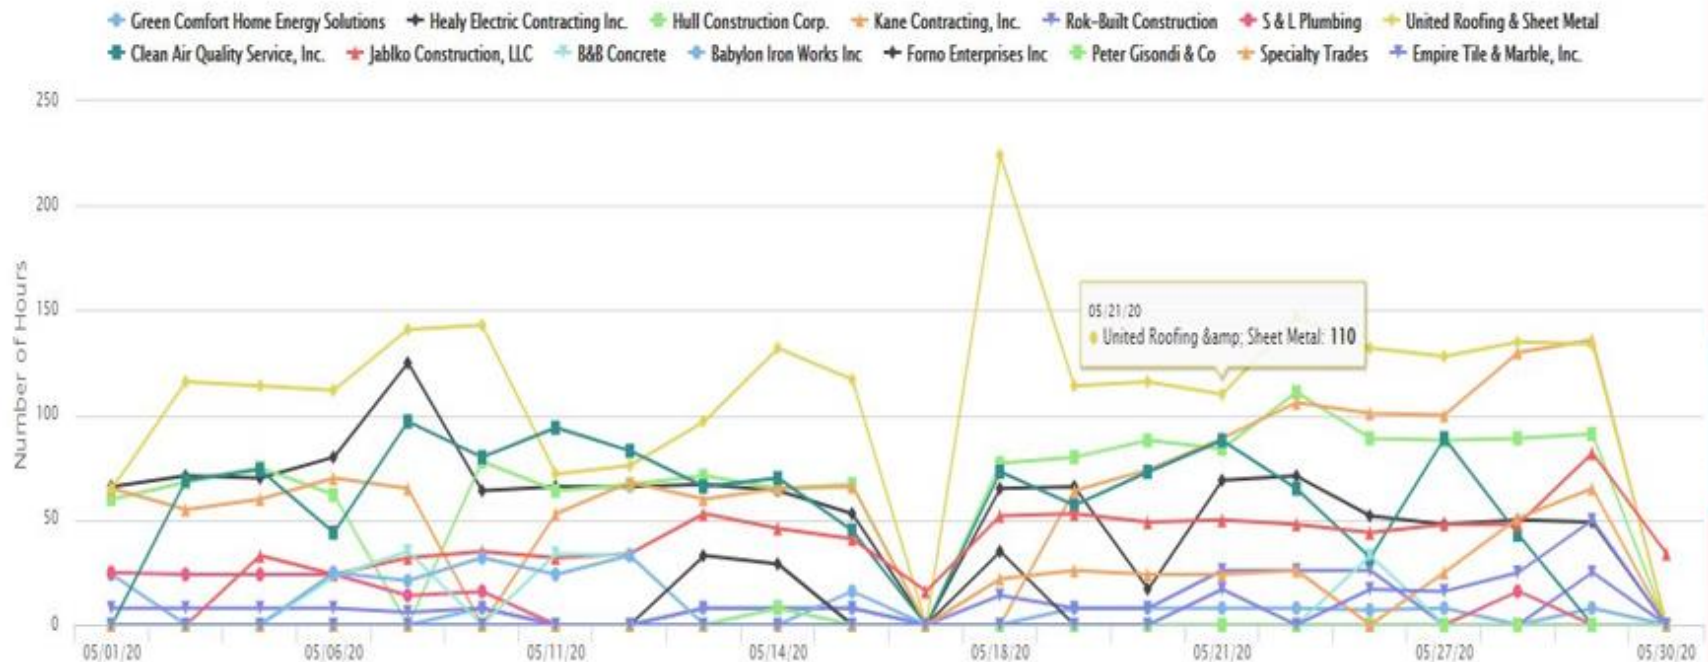




Scarsdale Union Free School District Summary of Daily Reports - Section IV Greenacres Elementary School - Additions & Alterations

Daily Log Manpower Report

▼ MANPOWER GRAPH

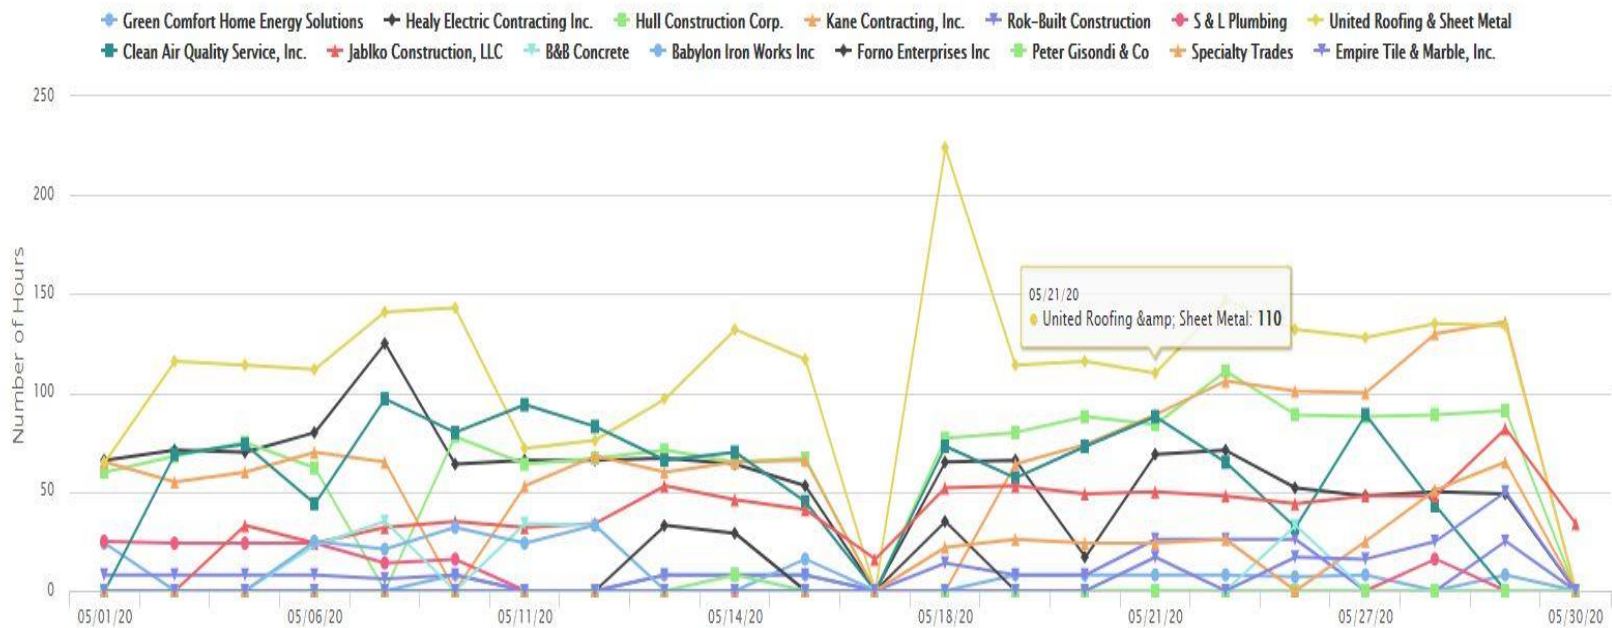


May 2020



Scarsdale Union Free School District Summary of Daily Reports - Section IV Heathcote, Quaker Ridge, & MS - Capital Improvements

Daily Log Manpower Report

▼ MANPOWER GRAPH

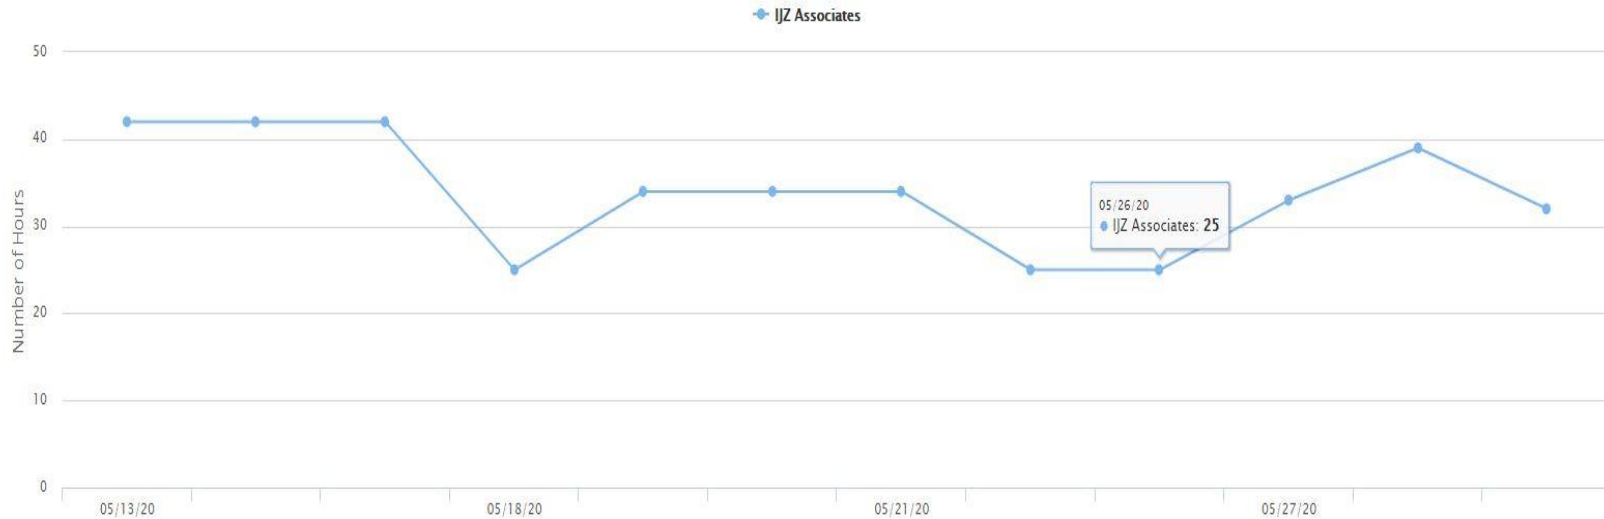


May 2020



Scarsdale Union Free School District Summary of Daily Reports - Section IV Edgewood & Fox Meadow - HVAC & Interior Alterations

Daily Log Manpower Report

▼ MANPOWER GRAPH

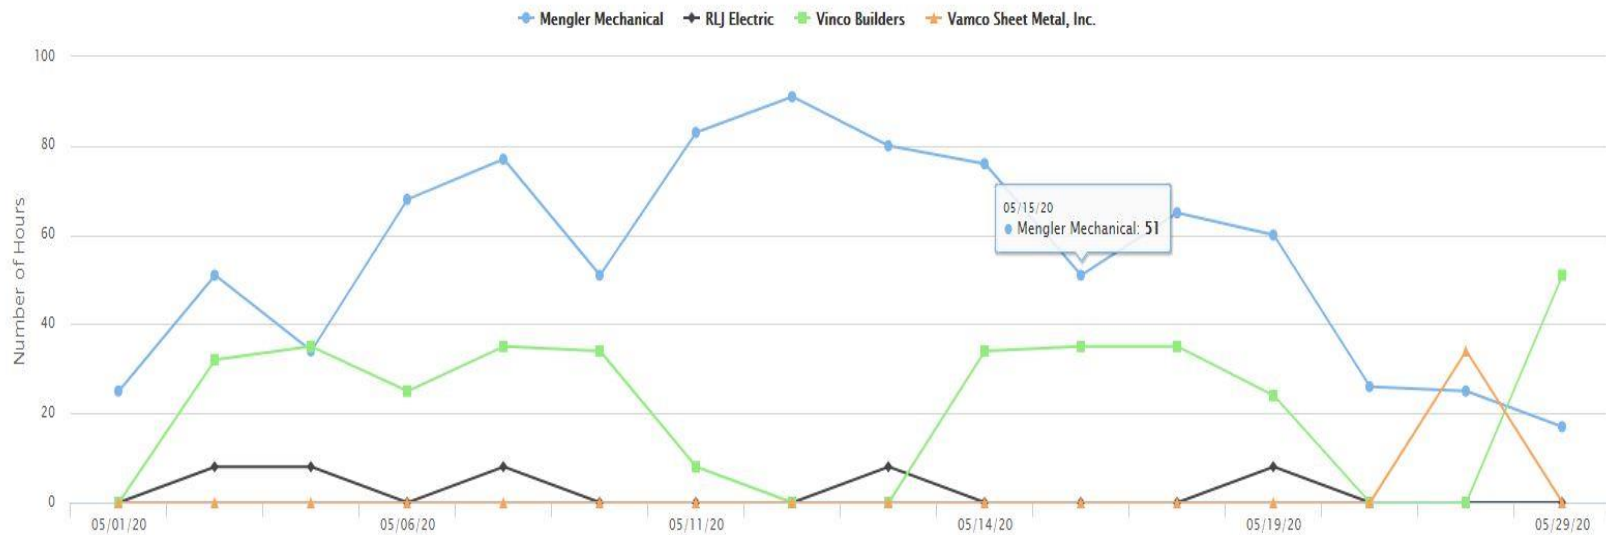

May 2020
