



SCARSDALE
PUBLIC SCHOOLS

November 2019 Construction Report



PEC

PARK EAST CONSTRUCTION

Prepared by Francesco V. Borgese



Table of Contents

▶ **Section I - Work Progress through the Month of November**

Greenacres Elementary School (Addition and Alterations)

Scarsdale High School (Boiler Replacement)

District Wide (Security Vestibules)

▶ **Section II - Planned work for the month of December**

▶ **Section III - Progress Photos**

▶ **Section IV - Summary of Daily Reports**



Scarsdale Union Free School District Progress Report - Section I Greenacres Elementary School

Work Progress - Greenacres Elementary School Addition (Phase - 1)

- ▶ New addition foundation / footing excavation - 90% Complete
- ▶ New addition footing rebar and formwork - 90% Complete
- ▶ New addition concrete footings - 90% Complete
- ▶ New addition foundation walls rebar and form work - 90% Complete
- ▶ New addition concrete foundation walls - 90% Complete
- ▶ New addition CMU partitions - 5% Complete
- ▶ New Addition face brick masonry - 5% Complete
- ▶ Below grade plumbing storm drainage piping - 85% Complete
- ▶ Below grade sanitary piping - 85% Complete
- ▶ Structural steel erection - 15% Complete
- ▶ **1st Floor slab preparation - 5% Complete**



**Scarsdale Union Free School District
Progress Report - Section I
Scarsdale HS - Boiler Replacement
District Wide - Security Vestibules**

Work Progress - Scarsdale High School

- ▶ Programming and Commissioning - Complete

Work Progress - Edgewood Elementary School

- ▶ Programming of card access - Complete

Work Progress - Fox Meadow Elementary School

- ▶ Programming of card access - Complete

Work Progress - Greenacres Elementary School

- ▶ Programming of card access - Complete

Work Progress - Heathcote Elementary School

- ▶ Programming of card access - Complete

Work Progress - Quaker Ridge Elementary School

- ▶ Programming of card access - Complete



**Scarsdale Union Free School District
Progress Report - Section II
Greenacres Elementary School**

**Planned Work for December
Greenacres Elementary School Addition (Phase - I)**

- ▶ Complete remaining addition footings and foundation walls.
- ▶ Pour portion of concrete floor slab (Multi Purpose Room / Learning Commons).
- ▶ Mark out and create openings for HVAC equipment in metal decking.
- ▶ Begin installation of plumbing hangers at underside of metal decking.
- ▶ Continue construction of CMU partitions.
- ▶ Continue construction of face brick masonry.



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



**Structural Steel Erection (Sage
Terrace & Huntington Avenue)**



**Structural Steel Erection (Sage
Terrace & Huntington Avenue)**

November 2019



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



**Installation of foundation wall rebar
at Stair 163 & Exterior Storage AA2**



**Installation of foundation wall rebar
at Stair 163 & Exterior Storage AA2**

November 2019



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



**Forming foundation wall at Stair
163 & Exterior Storage AA2**



**Forming foundation wall at Stair
163 & Exterior Storage AA2**

November 2019



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



**Construction of CMU partitions
along Sage Terrace**



**Construction of CMU partitions
along Sage Terrace**



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**




Construction of CMU partition at
proposed Storage Room 151.



Construction of CMU partition at
proposed Multi Purpose Room
(between proposed addition &
existing building).



Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I

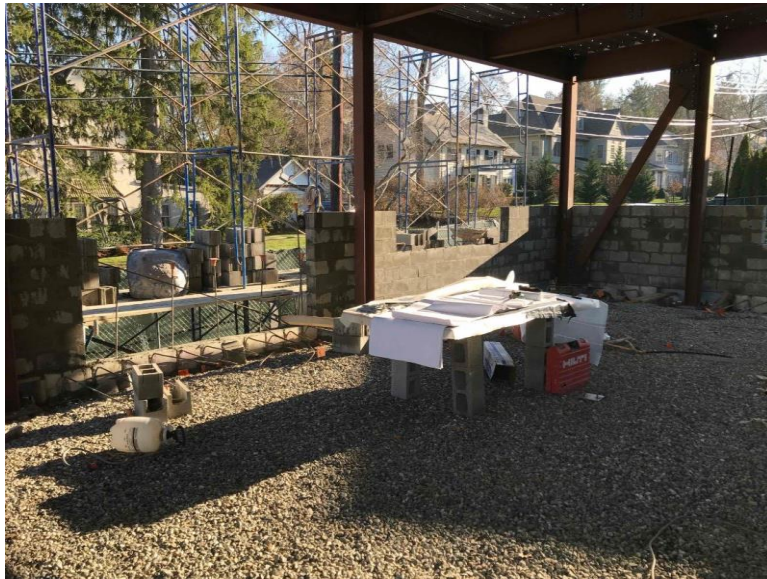

CMU construction & stone base preparation for slab at proposed Multi Purpose Room.



CMU construction & stone base preparation for slab at proposed Multi Purpose Room.



Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I



Installation of proposed below grade electrical conduit (between proposed addition & existing building).

November 2019




Installation of below grade plumbing sanitary piping.



Scarsdale Union Free School District Summary of Daily Reports - Section IV Greenacres Elementary School - Additions & Alterations

Daily Log Manpower Report

▼ MANPOWER GRAPH

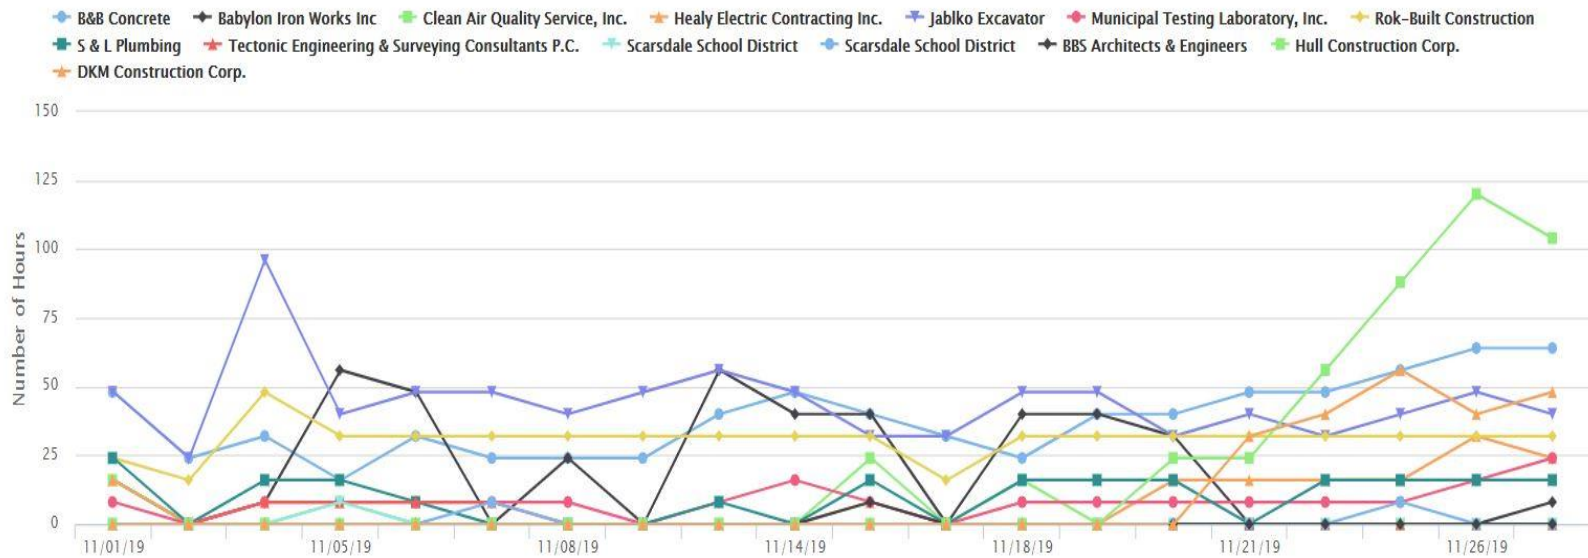

November 2019
