



SCARSDALE
PUBLIC SCHOOLS

October 2019 Construction Report



PARK EAST CONSTRUCTION

Prepared by Francesco V. Borgese



Table of Contents

▶ **Section I - Work Progress through the Month of September**

Greenacres Elementary School	(Addition and Alterations)
Heathcote Elementary School	(Roof Replacement)
Scarsdale High School	(Boiler Replacement)
District Wide	(Security Vestibules)

▶ **Section II - Planned work for the month of October**

▶ **Section III - Progress Photos**

▶ **Section IV - Summary of Daily Reports**



Scarsdale Union Free School District Progress Report - Section I Greenacres Elementary School

Work Progress - Greenacres Elementary School Addition (Phase - 1)

- ▶ New addition foundation / footing excavation - 75% Complete
- ▶ New addition footing rebar and formwork - 70% Complete
- ▶ New addition concrete footings - 65% Complete
- ▶ New addition foundation walls rebar and form work - 70% Complete
- ▶ New addition concrete foundation walls - 65% Complete
- ▶ Below grade plumbing storm drainage piping - 60% Complete
- ▶ Below grade sanitary piping - 60% Complete



**Scarsdale Union Free School District
Progress Report - Section I
Heathcote E.S. - Roof Replacement
Scarsdale HS - Boiler Replacement
District Wide - Security Vestibules**

Work Progress - Heathcote Elementary School

- ▶ Punch list - Complete

Work Progress - Scarsdale High School

- ▶ Boiler BMS controls - Complete
- ▶ Programming and Commissioning - 90% Complete

Work Progress - Edgewood Elementary School

- ▶ Programming of card access - In Progress
- ▶ Relocation of fire alarm devices - In Progress

Work Progress - Fox Meadow Elementary School

- ▶ Programming of card access - In Progress
- ▶ Relocation of fire alarm devices - In Progress



Scarsdale Union Free School District Progress Report - Section I District Wide Security Vestibules

Work Progress - Greenacres Elementary School

- ▶ Programming of card access - In Progress
- ▶ Relocation of fire alarm devices - In Progress

Work Progress - Heathcote Elementary School

- ▶ Installation of overhead cabinet heater - Complete
- ▶ Programming of card access - In Progress

Work Progress - Quaker Ridge Elementary School

- ▶ Installation of overhead cabinet heater - Complete
- ▶ Programming of card access - In Progress



**Scarsdale Union Free School District
Progress Report - Section II
Greenacres Elementary School**

Planned Work for November - Greenacres Elementary School Addition (Phase - I)

- ▶ Continue excavation for proposed addition footings
- ▶ Continue installation of rebar and formwork for proposed addition footings and foundations
- ▶ Continue pouring concrete for proposed addition footings and foundations
- ▶ Continue below grade plumbing roughing (sanitary and storm drainage piping)
- ▶ Deliver and begin erecting structural steel



**Scarsdale Union Free School District
Progress Report - Section II
Scarsdale High School - Boiler Replacement
District Wide - Security Vestibules**

Planned Work for November - Scarsdale High School

- ▶ Provide training on new boilers and system.
- ▶ Punch list.

Planned Work for November - District Wide Security Vestibules

- ▶ Complete card access programming .
- ▶ Complete fire alarm relocation at Fox Meadow, Edgewood, and Greenacres.



Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I



Spreading stone at area of new addition (Sage Terrace & Huntington Avenue)



Poured Concrete footing along Huntington Avenue

October 2019



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



Poured concrete foundation wall at proposed storage room.



Poured concrete foundation wall at proposed storage room.



Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I



Removal of forms at newly poured wall adjacent to existing gymnasium.



Poured concrete footing and pier adjacent to proposed cafeteria / kitchen area.



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



Removal of formwork at proposed concrete foundation walls and pier.



Removal of formwork at poured concrete foundation wall between proposed corridor at proposed kitchen.



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**



Removal of formwork at proposed concrete foundation.



Construction of formwork for proposed foundation walls.



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**




Installation of below grade plumbing piping.



Installation of below grade plumbing piping.



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School - Addition Phase I**

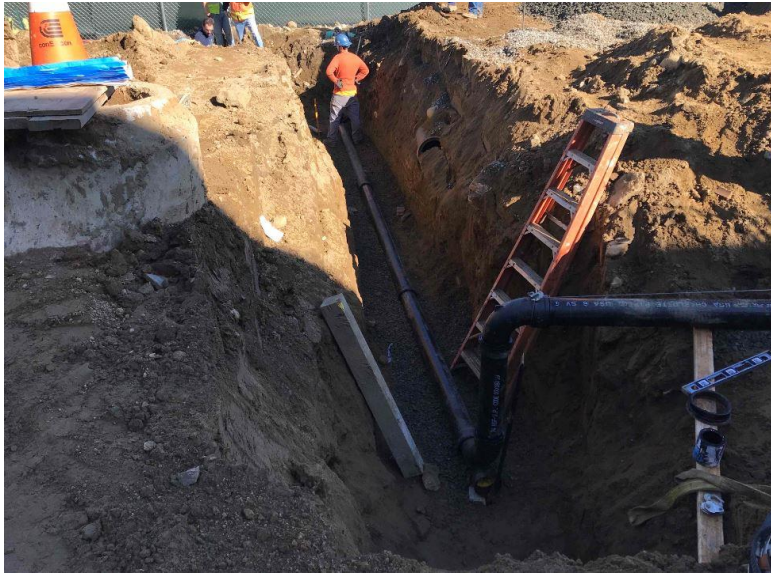

Installation of below grade plumbing piping.




Installation of below grade plumbing piping.



Scarsdale Union Free School District Summary of Daily Reports - Section IV Greenacres Elementary School - Additions & Alterations

Daily Log Manpower Report

▼ MANPOWER GRAPH

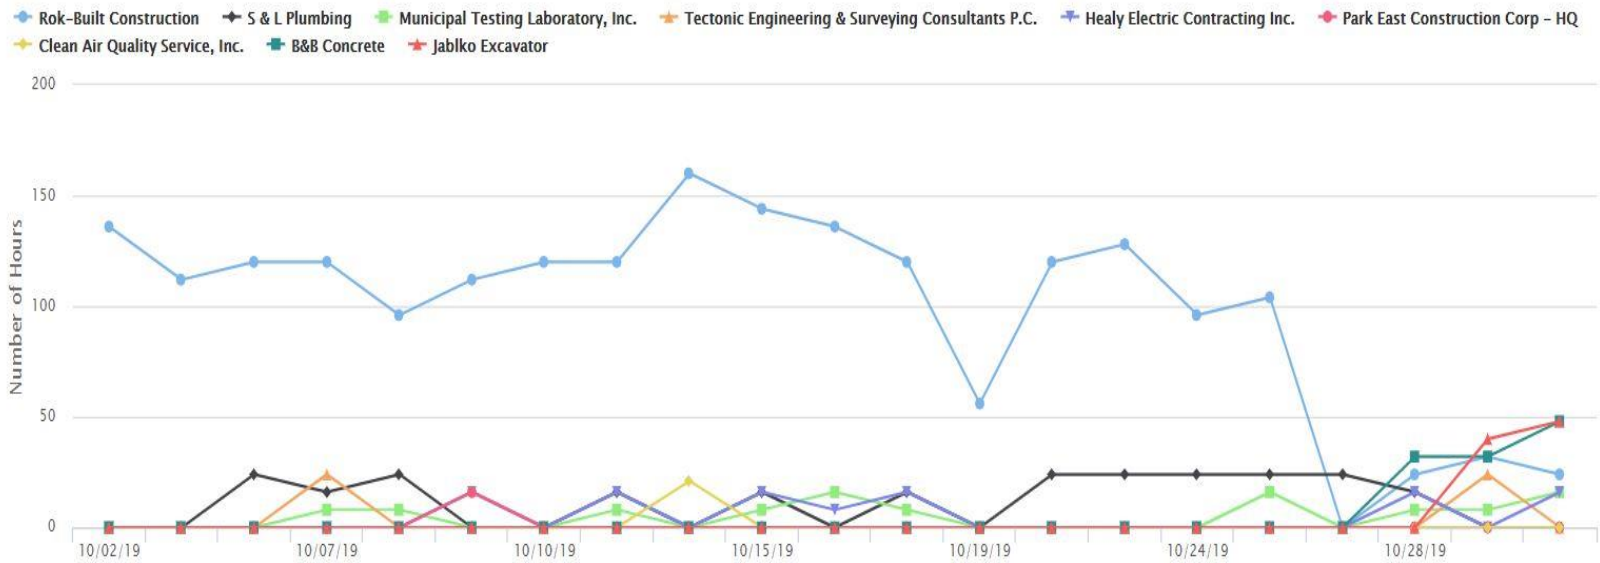

October 2019
