




SCARSDALE
PUBLIC SCHOOLS

SEPTEMBER 2020 Construction Report

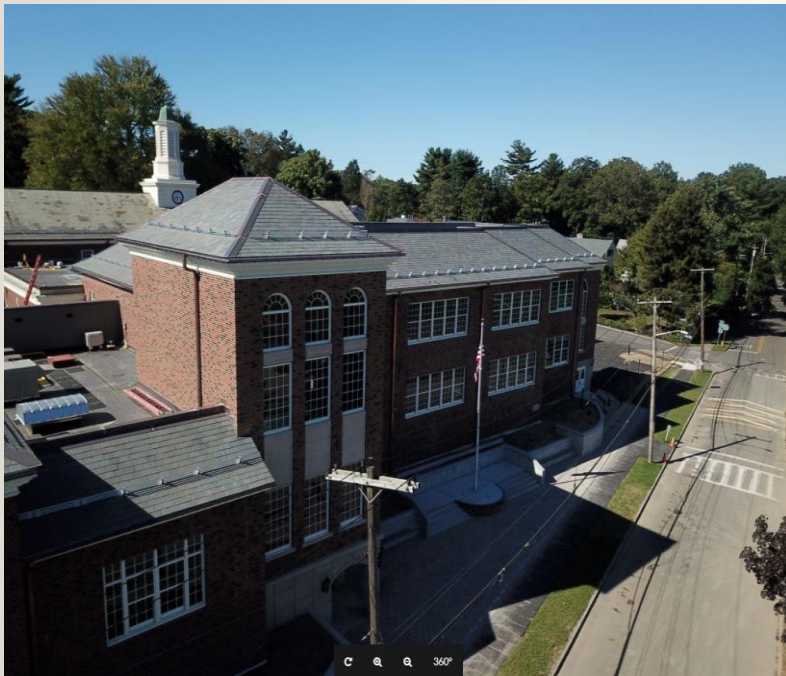

PEC

PARK EAST CONSTRUCTION

Prepared by Shawez Idrees



Table of Contents

▶ Section I - Work Progress through the month of September

Greenacres Elementary School	(Addition and Alterations)
Heathcote, Quaker Ridge, & MS	(Capital Improvements Project)
Edgewood	(HVAC and Interior Alterations)
Fox Meadow	(HVAC and Interior Alterations)
High School	(Phase 7 Capital Improvements)

▶ Section II - Planned work for the month of October

▶ Section III - Progress Photos

▶ Section IV - Summary of Daily Reports



Scarsdale Union Free School District Progress Report - Section I Greenacres Elementary School

Work Progress - Greenacres Elementary School Addition (Phase - 1)

- ▶ Exterior sitework - Complete

Work Progress - Greenacres Elementary School Existing Bldg. (Phase - 2)

- ▶ Installation of new casework - Complete
- ▶ Installation of new ceiling grid and finishes - Complete
- ▶ Installation of new light fixtures - Complete
- ▶ Installation of new flooring finishes - Complete
- ▶ Installation of new ceramic wall / floor tiles - Complete
- ▶ Installation of new plumbing fixtures - Complete
- ▶ Startup of new boilers - Complete



**Scarsdale Union Free School District
Progress Report - Section I
HC, QR, MS - Capitol Improvements Project**

Work Progress - Quaker Ridge Elementary School

- ▶ **Punchlist**

Work Progress - Quaker Ridge Elementary School

- ▶ **Punchlist**

Work Progress - Quaker Ridge Elementary School

- ▶ **Punchlist**



**Scarsdale Union Free School District
Progress Report - Section I
Edgewood & Fox Meadow - HVAC & Interior Alterations Project**

Work Progress - Edgewood Elementary School

- ▶ Startup of new boilers - Complete
- ▶ Electrical service upgrades - 95% Complete
- ▶ Installation / connection of new ERV units - Complete

Work Progress - Fox Meadow Elementary School

- ▶ Installation of new ductwork within attic - Complete
- ▶ Startup of new boilers - Complete
- ▶ Electrical service upgrades - 95% Complete
- ▶ Installation / connection of new ERV units - Complete



Scarsdale Union Free School District Progress Report - Section I High School - Phase 7 Capital Improvements at HS Project

Work Progress - Scarsdale High School

GC Work Scope

- ▶ Rebuilding portion of existing stone wall - Complete
- ▶ Masonry repairs / repointing - Complete
- ▶ Foundation drainage / waterproofing - Complete
- ▶ Backfilling and site restoration - Complete
- ▶ Asphalt paving - Complete

Roof Work Scope

- ▶ Roofing replacement - Complete
- ▶ Detail / metal capping work - 90% Complete

Dean Field Work Scope

- ▶ Removal of existing trees - Complete
- ▶ Striping of existing field / soil - Complete
- ▶ Installation of field drainage - 90% Complete
- ▶ Grading and spreading of fill / topsoil - 80% Complete



Scarsdale Union Free School District Planned Work - Section II District Wide

Planned Work for October

Greenacres Elementary School Addition (Phase - I & II)

- ▶ Address punch list items

Heathcote, Quaker Ridge, Middle School

- ▶ Address punch list items

Edgewood Elementary School

- ▶ Complete electrical upgrades
- ▶ Begin creating punch list

Fox Meadow Elementary School

- ▶ Complete electrical upgrades
- ▶ Begin creating punch list

Scarsdale High School

GC Work Scope

- ▶ Continue fabrication of existing stair handrails

Roof Work Scope

- ▶ Complete all detail metal capping work

Dean Field Work Scope

- ▶ Continue grading and prepping field for new natural turf.



Scarsdale Union Free School District Progress Pictures - Section III Greenacres Elementary School




Corner of Sage / Huntington



Sage Terrace Elevation



**Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School**

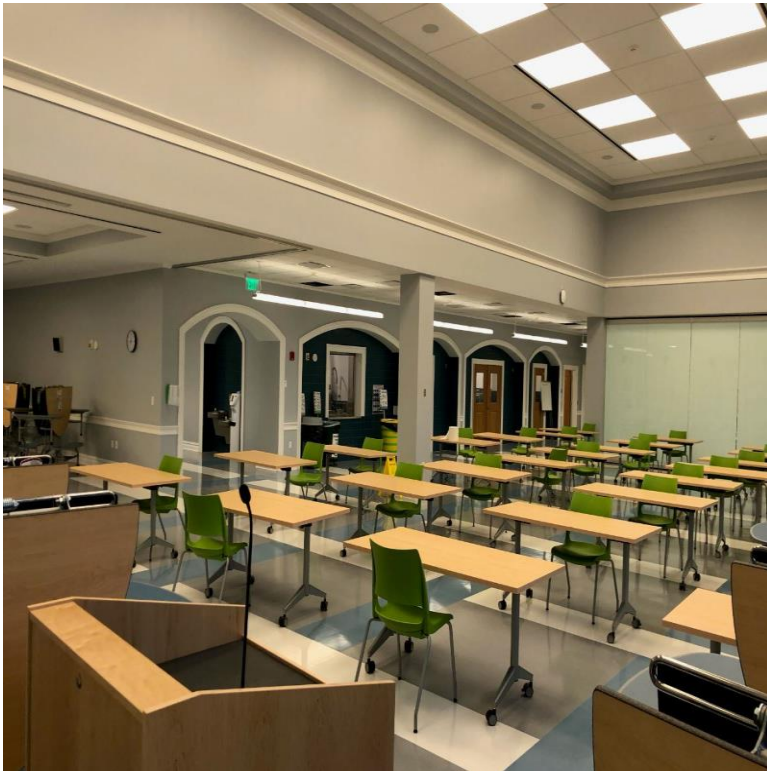

Learning Commons 146



Typical New Addition Classroom



Scarsdale Union Free School District
Progress Pictures - Section III
Greenacres Elementary School



Interior of staircase 163



Library




Scarsdale Union Free School District Progress Pictures - Section III Scarsdale High School



Roof Replacement



Scarsdale Union Free School District Progress Pictures - Section III Scarsdale High School

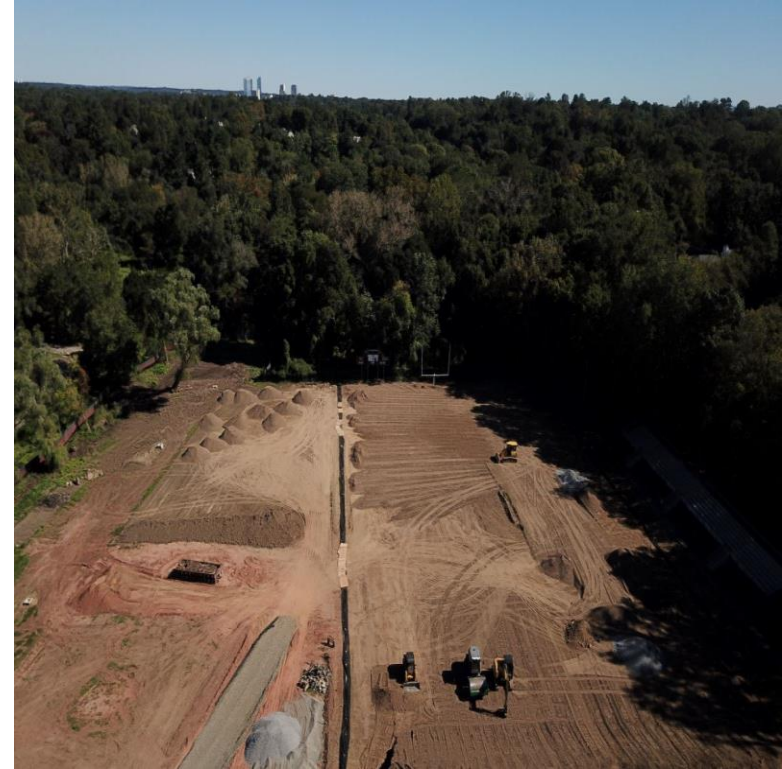

Dean Field Renovation



Scarsdale Union Free School District Progress Pictures - Section III Scarsdale High School




Walkway Replacement / Waterproofing



Scarsdale Union Free School District Progress Pictures - Section III Scarsdale High School



Masonry Repairs




Floor Joist / Flooring Tile
Replacement



Scarsdale Union Free School District Summary of Daily Reports - Section IV Greenacres Elementary School - Additions & Alterations

Daily Log Manpower Report

▼ MANPOWER GRAPH

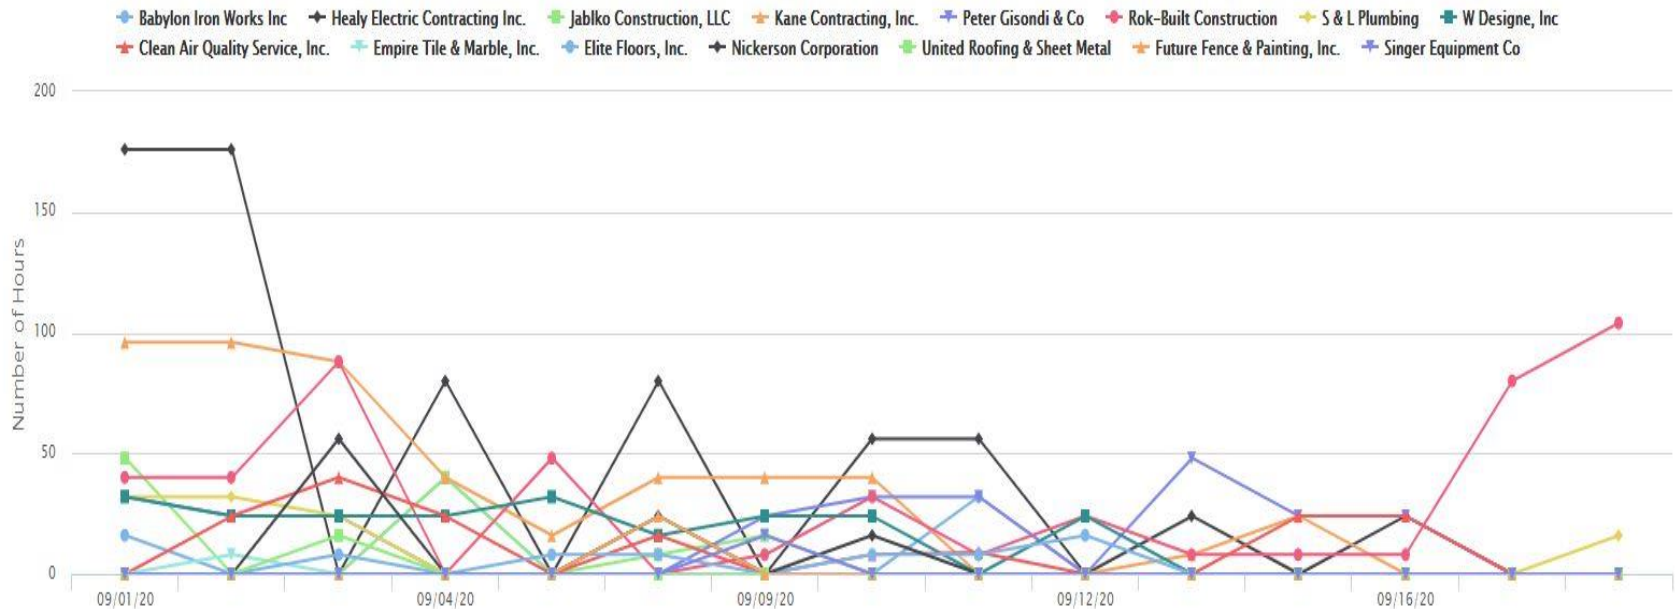




Scarsdale Union Free School District Summary of Daily Reports - Section IV Edgewood & Fox Meadow - HVAC & Interior Alterations

Daily Log Manpower Report

▼ MANPOWER GRAPH

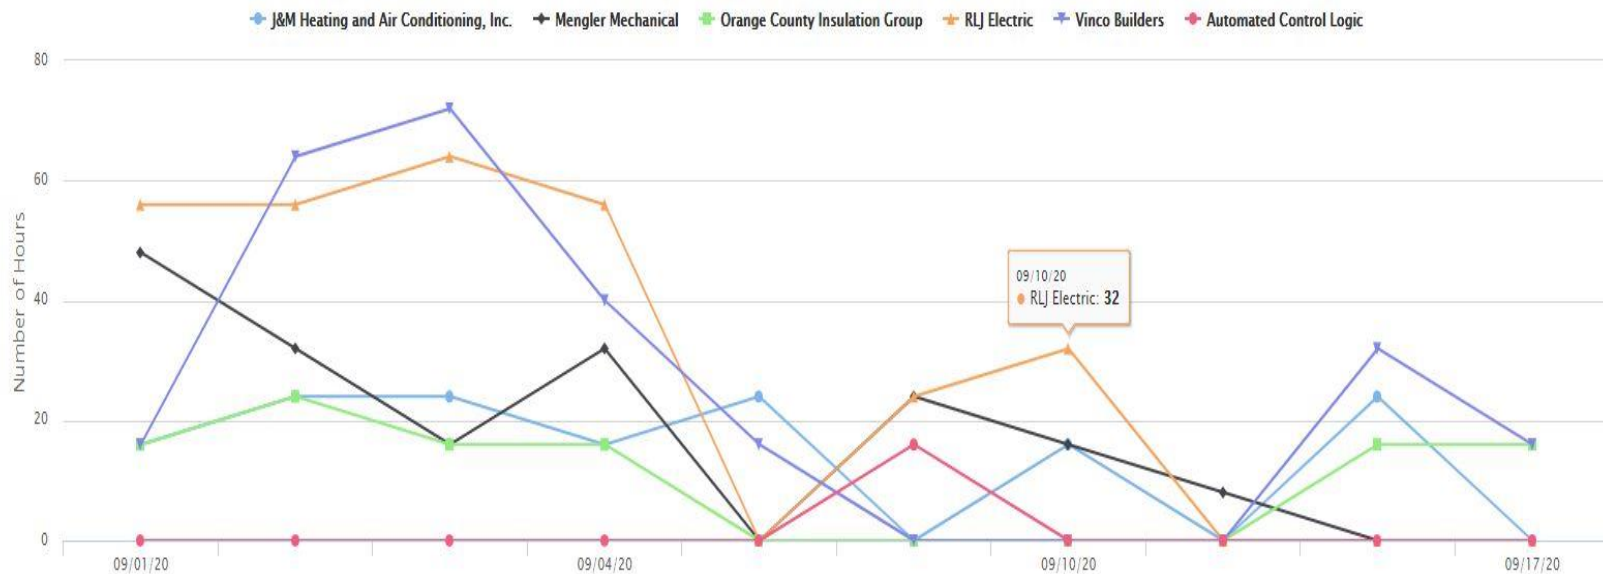



Scarsdale Union Free School District Summary of Daily Reports – Section IV Phase 7 Capital Improvements at High School

Daily Log Manpower Report

▼ MANPOWER GRAPH

